

156TH STREET PROJECT




PROJECT INFORMATION — AUGUST 2020

CONSTRUCTION UPDATE

Utility conflicts south of Bennington Road along Bennington Road have been cleared and construction is moving forward in the area. K2 Construction will focus on Bennington Road to the west of 156th Street for the time being. Utility relocation work will continue along 156th Street on the east side of Bennington Elementary School with OPPD installing buried power lines.

Updated phasing and schedules are provided below. These dates and timeframes are subject to change due to weather impacts or other unforeseen delays:

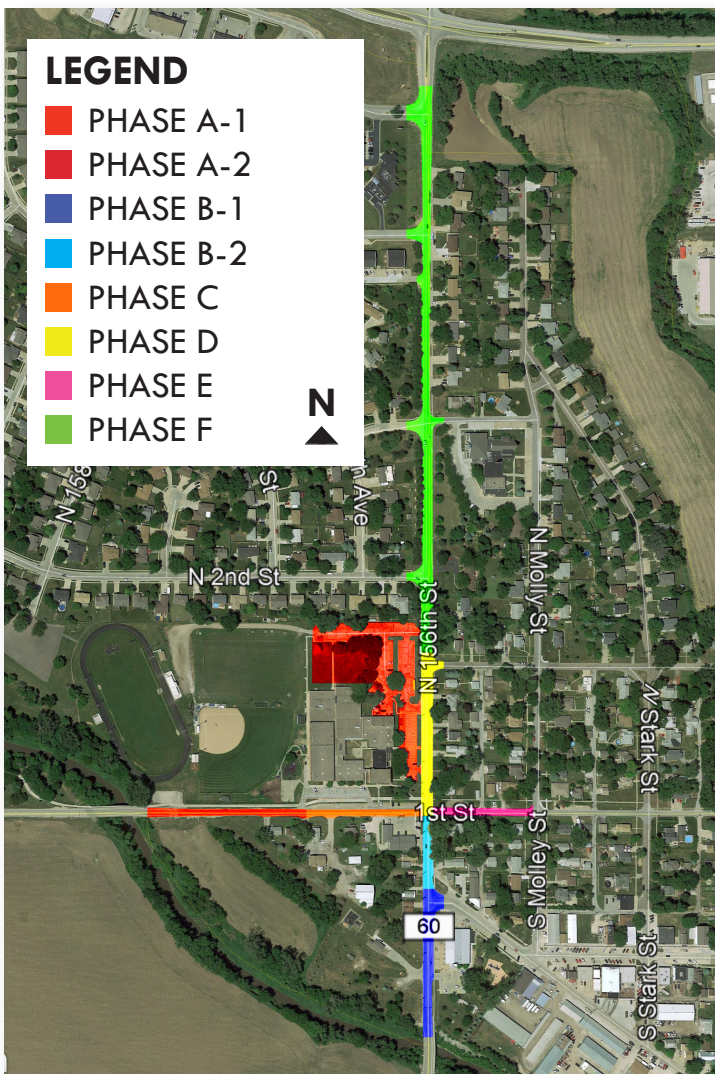

PHASES A-1 & A-2

Completed and open to school traffic

Area: Bennington Rd — Papio Creek Bridge to Bus Loop

Remaining Work: Lighting and landscape

PHASE C

Schedule: **7/29/20 to 8/19/20**

Closure: Bennington Rd — Bus Loop to 156th St

Detour: Military Rd/ 168th St/ Highway 36

PHASE B-1

Schedule: **7/6/20 to 8/28/20**

Closure: 156th St — Papio Creek Bridge to Warehouse St

Detour: Military Rd/ 168th St/ Highway 36

PHASE B-2

Schedule: **Started 8/11/20**

Closure: 156th St — Warehouse St to Bennington Rd

Detour: Military Rd/ 168th St/ Highway 36

ALL OTHER PHASES (D-F)

Schedule and order of work to be determined pending completion of other phases.

PROJECT CONTACTS

**Marvin Lech, NDOT District 2
Construction Engineer**
402-595-2534
marvin.lech@nebraska.gov

**Jeff Webert, K2 Construction
Project Manager**
402-467-2355 / 402-890-2299
jwebert@k2construction.biz

A Facebook group will be set up for the project. Please see the following for information:
facebook.com/groups/K2BenningtonProject/
