



156TH STREET PROJECT

PROJECT INFORMATION APRIL/MAY 2021

CONSTRUCTION UPDATE

Construction on 156th Street is starting to move forward now with better weather and utility conflicts addressed. The west side of 156th Street between Bennington Road and N 2nd Street/School Drive was poured on Tuesday and the east half is planned to be poured Friday (April 30th). The following few weeks will see construction on driveway approaches, sidewalks and finish grading in this area. Any changes to this pour schedule will delay the start of the next phase.

Since school is still in session, the contractor will skip over the N 2nd Street/School driveway intersection and start work at N Second Street (into Bennington Park neighborhood) on Monday May 3rd. Road closures will start around 8:45 am and will extend to Howard Lane. The Howard Lane intersection will remain open during this phase of work. Access to Bennington Elementary School will be via Howard Lane to Molly Street to N 2nd Street. The city is coordinating with the contractor to possibly allow right turns onto 156th Street from the school drive once the pavement has reached the required strength. This access will only be for the time needed for school drop offs and school pick ups daily until work on that segment of roadway is complete. **Access into the school lot is only allowed from N 2nd Street.**


Once school dismisses for the year on May 21st, the contractor will begin work on the intersection of N 2nd Street/School Driveway so it is completed well before school resumes in the fall. During this time, if access to the school is needed, it would be provided from the bus loop driveway to the parking lot. In addition, installation of the traffic signals at the intersection of 156th Street and Bennington Road will occur in June 2021 with the dismissal of school.


For any questions or concerns, please contact the project contacts or visit the project's Facebook page listed below.

PROJECT CONTACTS

Marvin Lech, NDOT District 2, Construction Engineer
402-595-2334
marvin.lech@nebraska.gov

Jeff Webert, K2 Construction, Project Manager
402-467-2355 / 402-890-2299
jwebert@k2construction.biz

 **A Facebook group has been set up for the project. Please see the following for information:**
facebook.com/groups/K2BenningtonProject/

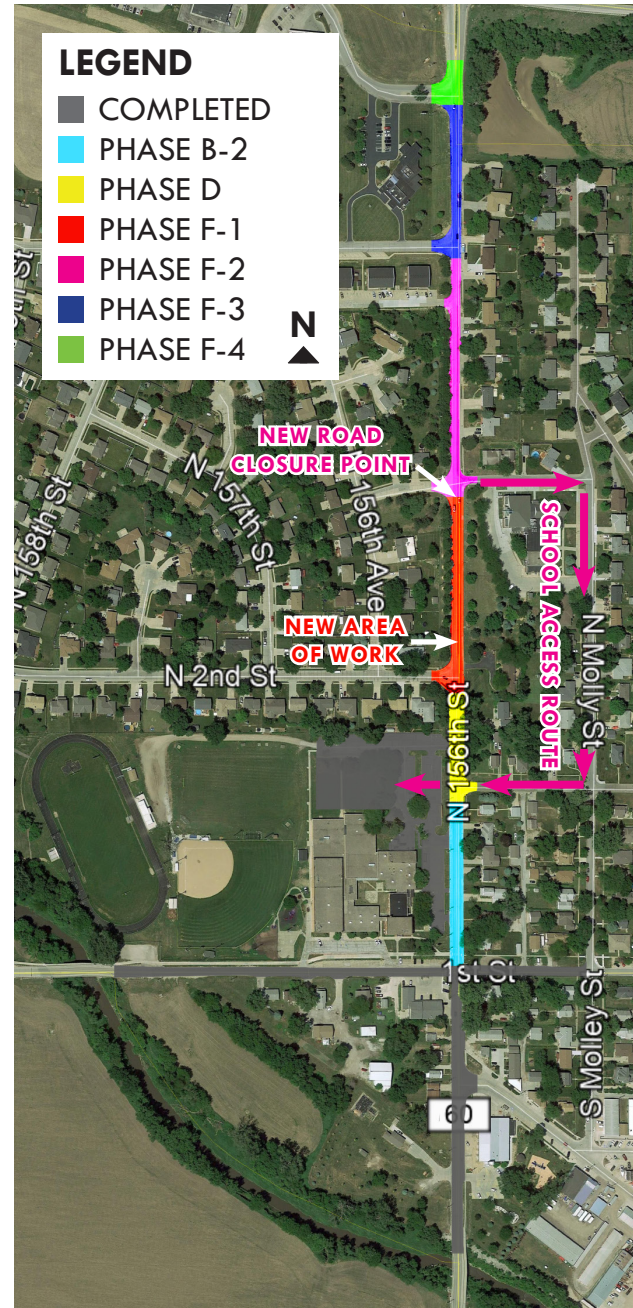

COMPLETED	Completed work open to school/ local traffic Area: Bennington Rd & 156th St south of Bennington Rd
PHASE B-2	Schedule: 3/8/21 to 5/21/21 Closure: 156th St - North of Bennington Rd to south of N 2nd St Detour: Bennington Rd/ 168th St/ Highway 36
PHASE D	Schedule: 5/24/21 to 6/18/21 Closure: Intersection of N 2nd St/ Bennington Elem. School driveway with 156th St Detour: Bennington Rd/ 168th St/ Highway 36
PHASE F-1	Schedule: 5/3/21 to 6/11/21 Closure: 156th St. from N Second St to Howard Lane
PHASE F-2	Schedule: 6/11/21 to 7/14/21 Closure: 156th St. from Howard Lane to 4th Street
PHASE F-3	Schedule: 7/15/21 to 8/5/21 Closure: 156th St. from 4th Street to CW Haden Dr
PHASE F-4	Schedule: 8/6/21 to 8/31/21 Closure: 156th St. CW Haden Drive intersection Detour: Bennington Road/168th Street/Highway 36
